



PT. SARANA TITIAN PERMATA

CLAIM SUMMARY

Contract No :

1. C&A. 1608.02/STP2 - 052

Type of Work	Unit	SPK Vol	Jan - Jul 2011 Claim	August Claim	Total Claimed (Jan - Aug 2011)	%
Excavator						
Main Drain 3,6x2,4x1,8	Meter	8,000.00	1,209.00	-	1,209.00	15.11%
Main Drain 2,4x1,8x1,2	Meter	-	-	-	-	-
Collection Drain 1,8x1,2x0,9	Meter	75,000.00	7,503.00	1,359.00	8,862.00	11.82%
Infield Drain 1,2x0,9x0,6	Meter	1,013,630.00	915,210.00	11,517.00	926,727.00	91.43%


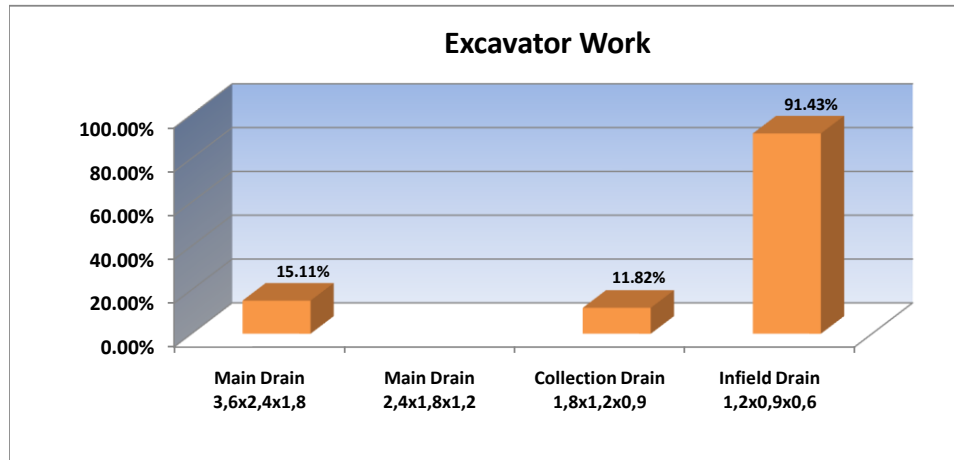


Chart & Detail Per Month

Type of Work	SPK Vol (Meter)	Progress	%
Main Drain 3,6x2,4x1,8	8,000.00	1,209.00	15.11%




Month	Monthly Progress	Accumulated
Jan-11	-	-
Feb-11	-	-
Mar-11	1,209.00	1,209.00
Apr-11	-	1,209.00
May-11	-	1,209.00
Jun-11	-	1,209.00
Jul-11	-	1,209.00
Aug-11	-	1,209.00
Total	1,209.00	

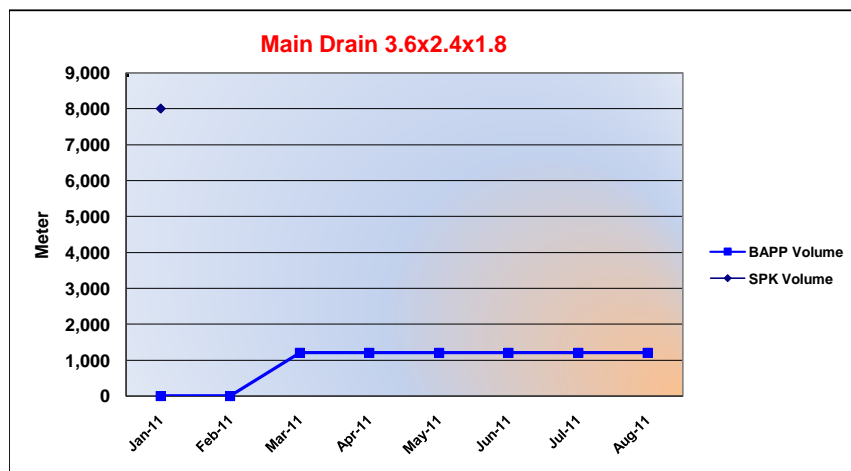

PT. SARANA TITIAN PERMATA


CLAIM SUMMARY

Type of Work	SPK Vol (Meter)	Progress	%
Main Drain 2,4x1,8x1,2	-	-	0.00%

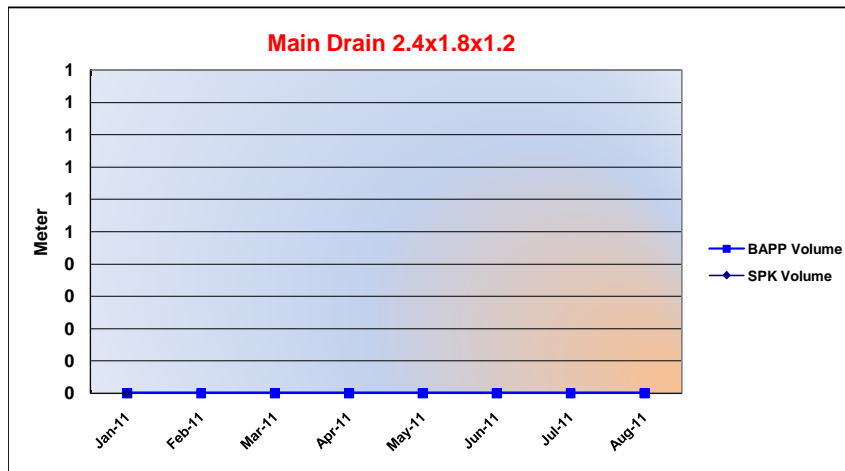


Month	Monthly Progress	Accumulated
Jan-11	-	-
Feb-11	-	-
Mar-11	-	-
Apr-11	-	-
May-11	-	-
Jun-11	-	-
Jul-11	-	-
Aug-11	-	-
Total	-	-

Type of Work	SPK Vol (Meter)	Progress	%
Collection Drain 1,8x1,2x0,9	75,000.00	8,862.00	11.82%

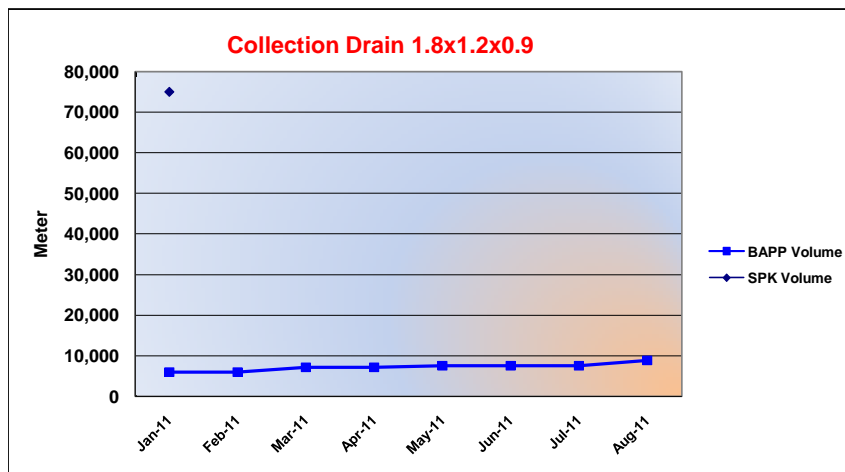

Month	Monthly Progress	Accumulated
Jan-11	5,947.00	5,947.00
Feb-11	-	5,947.00
Mar-11	1,206.00	7,153.00
Apr-11	-	7,153.00
May-11	350.00	7,503.00
Jun-11	-	7,503.00
Jul-11	-	7,503.00
Aug-11	1,359.00	8,862.00
Total	8,862.00	8,862.00

Type of Work	SPK Vol (Meter)	Progress	%
Infield Drain 1,2x0,9x0,6	1,013,630.00	926,727.00	91.43%

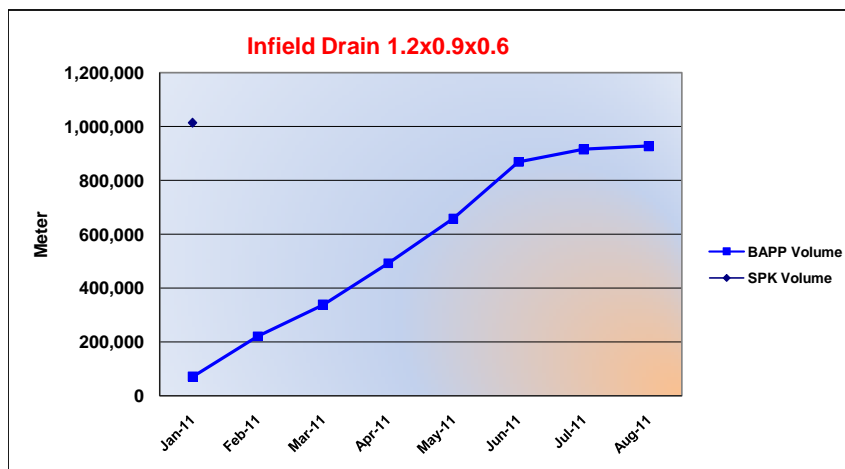

Month	Monthly Progress	Accumulated
Jan-11	70,669.00	70,669.00
Feb-11	149,954.00	220,623.00
Mar-11	117,166.00	337,789.00
Apr-11	153,975.00	491,764.00
May-11	165,201.00	656,965.00
Jun-11	211,178.00	868,143.00
Jul-11	47,067.00	915,210.00
Aug-11	11,517.00	926,727.00
Total	926,727.00	926,727.00



PT. SARANA TITIAN PERMATA

CLAIM SUMMARY
