





PT. KARUNIA KENCANA PERMAISEJATI

CLAIM SUMMARY KKP III

Contract No :
C&A. 1608.02/KKP3 - 070

Type of Work	Unit	SPK Vol	Feb - Jun 2011 Claim	July Claim	Total Claimed (Feb - Jul 2011)	%
Bulldozer						
Stacking Bulldozer - Low Vegetation	Ha	368.20	-	20.55	20.55	5.58%
Excavator						
Stacking Excavator	Ha	157.80	63.50	21.24	84.74	53.70%
Road Formation 8 M	Meter	5,260.00	859.00	221.00	1,080.00	20.53%
Road Formation 6 M	Meter	26,300.00	1,894.00	1,598.00	3,492.00	13.28%
Main Drain 2,4x1,8x1,2	Meter	2,630.00	-	-	-	0.00%
Collection Drain 1,8x1,2x0,9	Meter	13,150.00	5,808.00	1,262.00	7,070.00	53.76%
Infield Drain 1,2x0,9x0,6	Meter	81,512.00	19,964.00	16,794.00	36,758.00	45.10%
Underbrushing (Imas)	Ha	526.00	63.50	41.79	105.29	20.02%
Felling (Tumbang)	Ha	526.00	63.50	41.79	105.29	20.02%

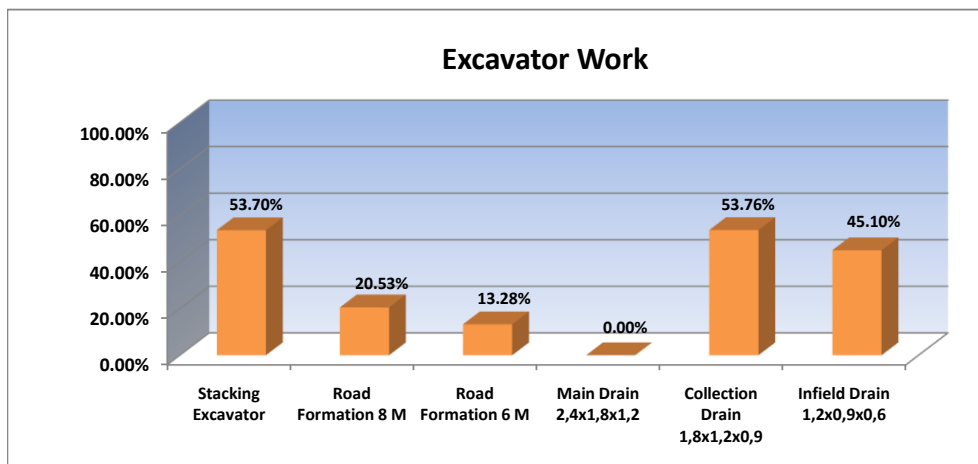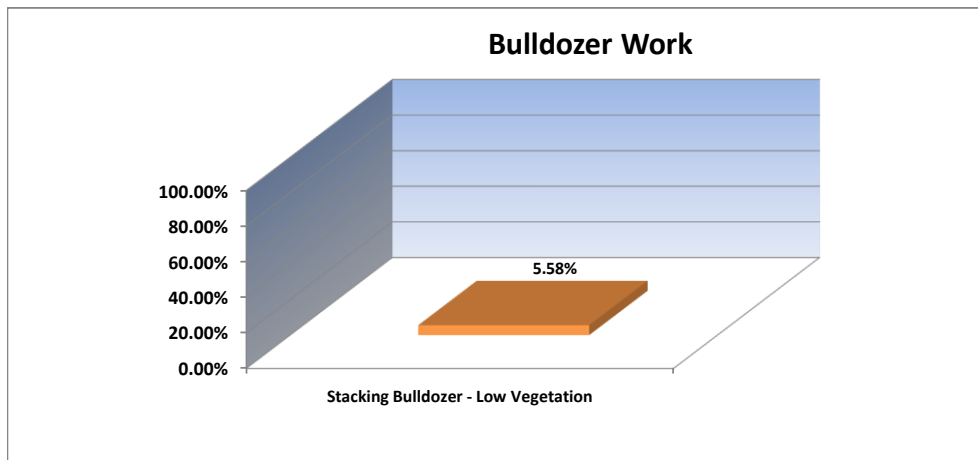



CLAIM SUMMARY KKP III


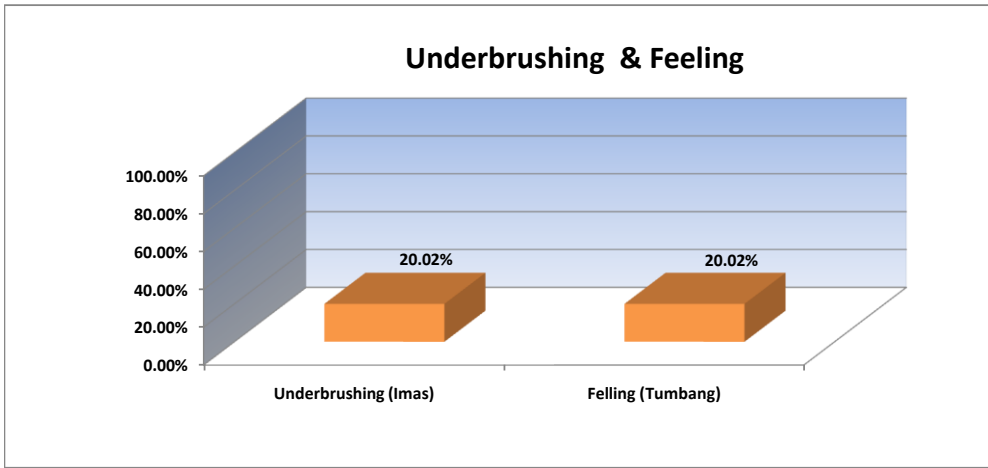



Chart & Detail Per Month

Type of Work	SPK Vol (Ha)	Progress	%
Stacking Bulldozer - Low Vegetation	368.20	20.55	5.58%

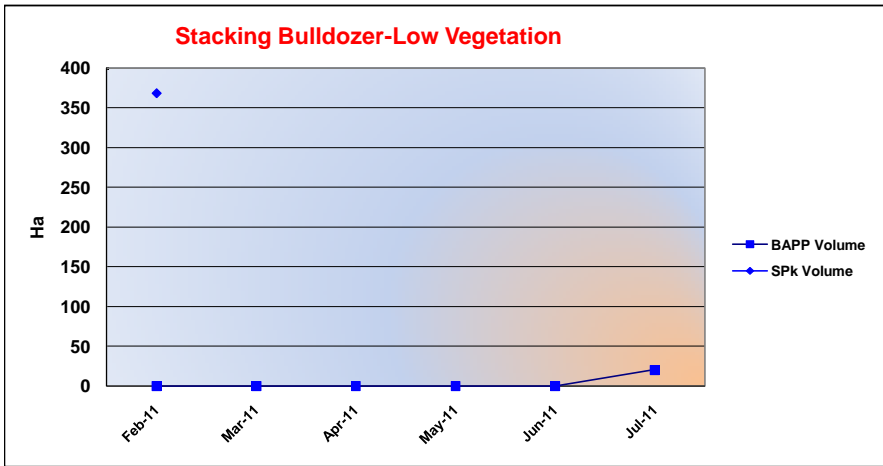

Month	Monthly Progress	Accumulated
Feb-11	-	-
Mar-11	-	-
Apr-11	-	-
May-11	-	-
Jun-11	-	-
Jul-11	20.55	20.55
Total	20.55	

Type of Work	SPK Vol (Ha)	Progress	%
Stacking Excavator	157.80	84.74	53.70%

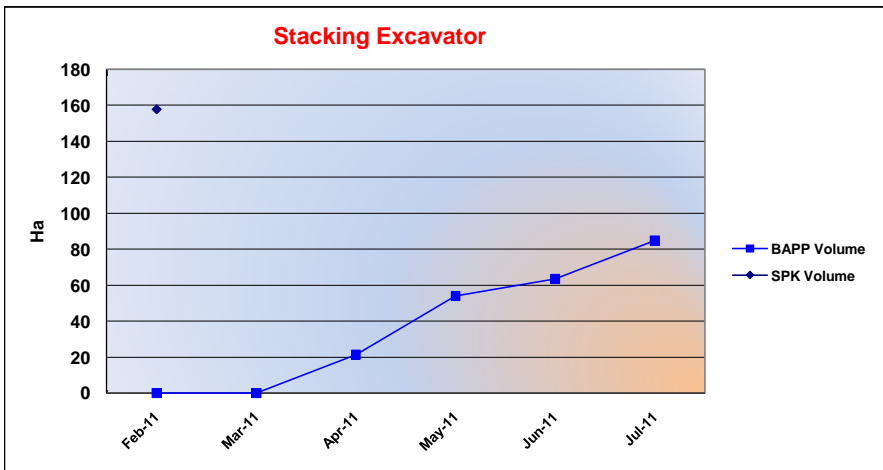


Month	Monthly Progress	Accumulated
Feb-11	-	-
Mar-11	-	-
Apr-11	21.35	21.35
May-11	32.67	54.02
Jun-11	9.48	63.50
Jul-11	21.24	84.74
Total	84.74	



PT. KARUNIA KENCANA PERMAISEJATI


CLAIM SUMMARY KKP III

Type of Work	SPK Vol (Meter)	Progress	%
Road Formation 8 M	5,260.00	1,080.00	20.53%

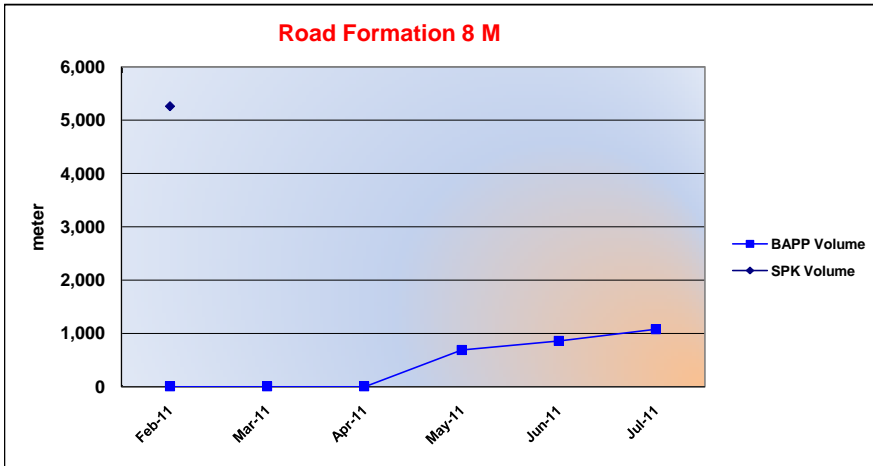


Month	Monthly Progress	Accumulated
Feb-11	-	-
Mar-11	-	-
Apr-11	-	-
May-11	689.00	689.00
Jun-11	170.00	859.00
Jul-11	221.00	1,080.00
Total	1,080.00	

Type of Work	SPK Vol (Meter)	Progress	%
Road Formation 6 M	26,300.00	3,492.00	13.28%

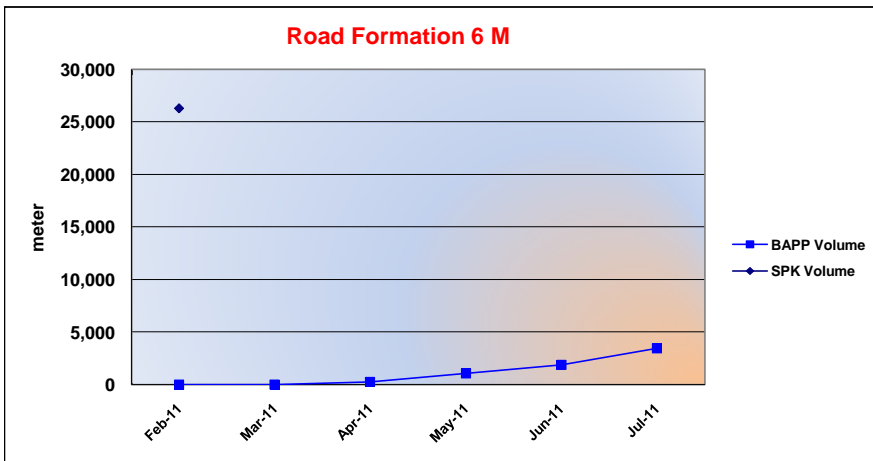

Month	Monthly Progress	Accumulated
Feb-11	-	-
Mar-11	-	-
Apr-11	249.00	249.00
May-11	849.00	1,098.00
Jun-11	796.00	1,894.00
Jul-11	1,598.00	3,492.00
Total	3,492.00	

Type of Work	SPK Vol (Meter)	Progress	%
Main Drain 2,4x1,8x1,2	2,630.00	-	0.00%

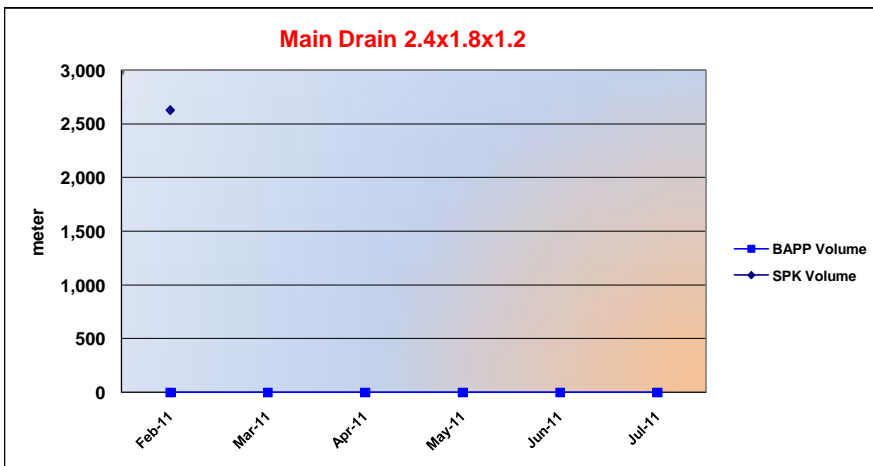


Month	Monthly Progress	Accumulated
Feb-11	-	-
Mar-11	-	-
Apr-11	-	-
May-11	-	-
Jun-11	-	-
Jul-11	-	-
Total	-	



PT. KARUNIA KENCANA PERMAISEJATI


CLAIM SUMMARY KKP III

Type of Work	SPK Vol (Meter)	Progress	%
Collection Drain 1,8x1,2x0,9	13,150.00	7,070.00	53.76%

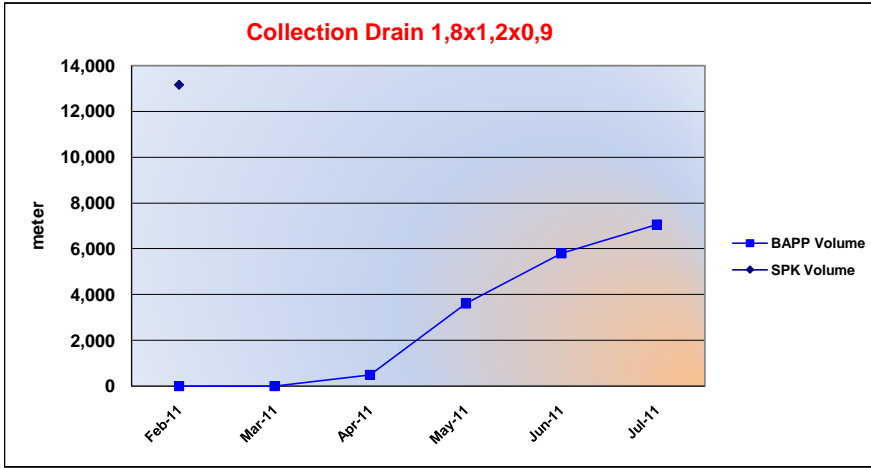


Month	Monthly Progress	Accumulated
Feb-11	-	-
Mar-11	-	-
Apr-11	499.00	499.00
May-11	3,118.00	3,617.00
Jun-11	2,191.00	5,808.00
Jul-11	1,262.00	7,070.00
Total	7,070.00	

Type of Work	SPK Vol (Meter)	Progress	%
Infield Drain 1,2x0,9x0,6	81,512.00	36,758.00	45.10%

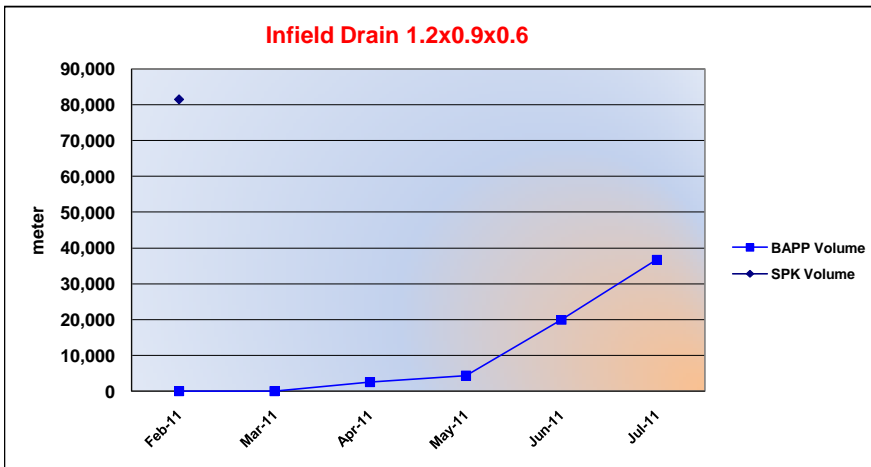

Month	Monthly Progress	Accumulated
Feb-11	-	-
Mar-11	-	-
Apr-11	2,560.00	2,560.00
May-11	1,738.00	4,298.00
Jun-11	15,666.00	19,964.00
Jul-11	16,794.00	36,758.00
Total	36,758.00	

Type of Work	SPK Vol (Ha)	Progress	%
Underbrushing (Imas)	526.00	105.29	20.02%

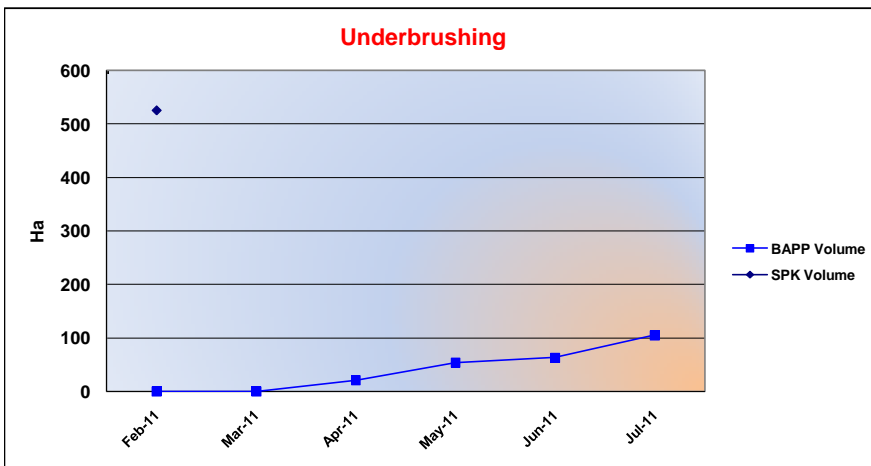


Month	Monthly Progress	Accumulated
Feb-11	-	-
Mar-11	-	-
Apr-11	21.35	21.35
May-11	32.67	54.02
Jun-11	9.48	63.50
Jul-11	41.79	105.29
Total	105.29	



PT. KARUNIA KENCANA PERMAISEJATI

CLAIM SUMMARY KKP III

Type of Work	SPK Vol (Ha)	Progress	%
Felling (Tumbang)	526.00	105.29	20.02%

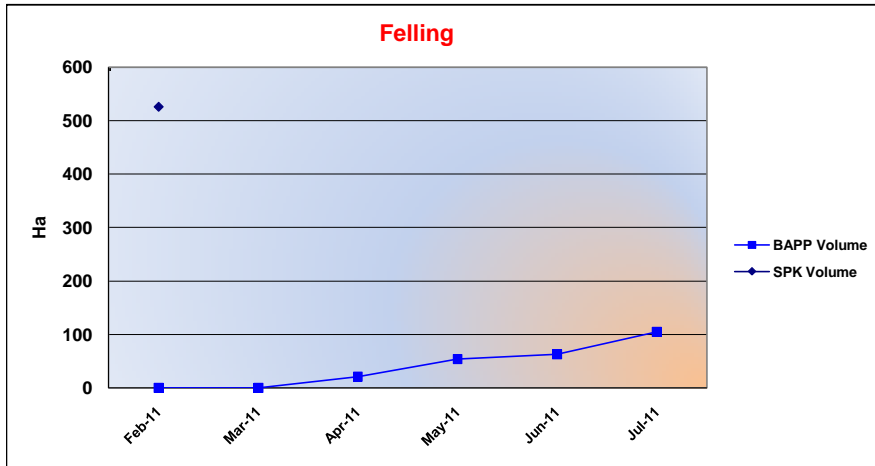

Month	Monthly Progress	Accumulated
Feb-11	-	-
Mar-11	-	-
Apr-11	21.35	21.35
May-11	32.67	54.02
Jun-11	9.48	63.50
Jul-11	41.79	105.29
Total	105.29	
