





PT. RIMBA HARAPAN SAKTI

CLAIM SUMMARY

Contract No :

1. C&A. 1608.02/RHS - 020

Type of Work	Unit	SPK Vol	Jan - Mar 2011 Claim	April Claim	Total Claimed (Jan - Apr 2011)	%
Bulldozer						
Stacking Bulldozer	Ha	200.00	-	-	-	0.00%
Excavator						
Stacking Excavator	Ha	500.00	49.90	76.92	126.82	25.36%
Road Formation 8 M	Meter	7,000.00	-	-	-	0.00%
Road Formation 6 M	Meter	35,000.00	474.00	-	474.00	1.35%
Main Drain 3,6x2,4x1,8	Meter	8,100.00	1,185.00	-	1,185.00	14.63%
Main Drain 2,4x1,8x1,2	Meter	27,000.00	8,847.00	482.00	9,329.00	34.55%
Collection Drain 1,8x1,2x0,9	Meter	130,000.00	26,298.00	-	26,298.00	20.23%
Infield Drain 1,2x0,9x0,6	Meter	1,782,000.00	803,595.00	161,915.00	965,510.00	54.18%
Underbrushing (Imas)	Ha	700.00	461.42	76.92	538.34	76.91%

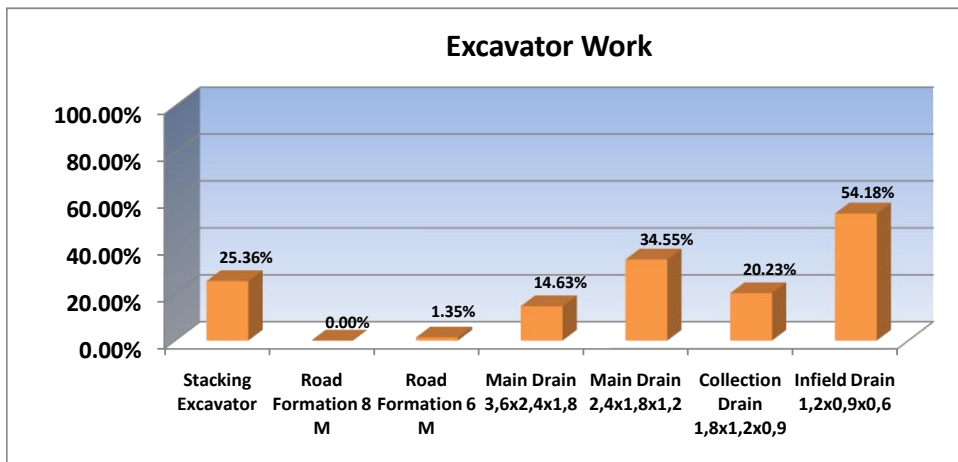



PT. RIMBA HARAPAN SAKTI

CLAIM SUMMARY


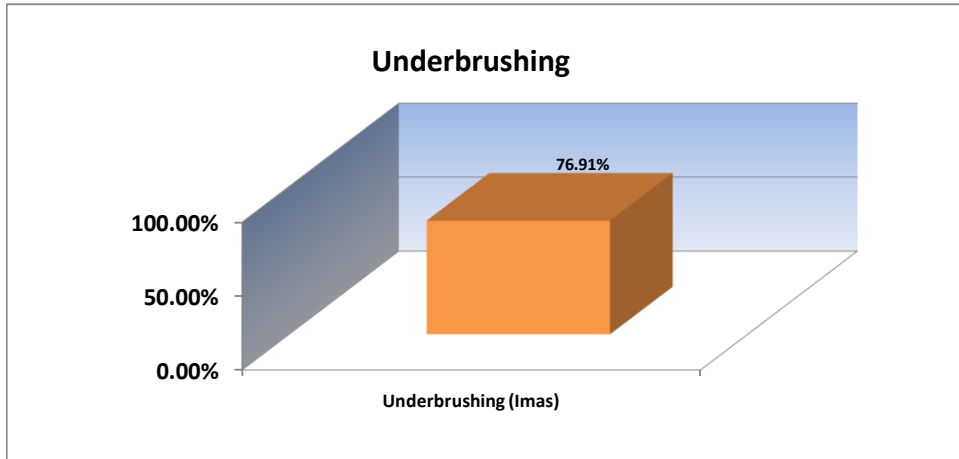



Chart & Detail Per Month

Type of Work	SPK Vol (Ha)	Progress	%
Stacking Bulldozer	200.00	-	0.00%

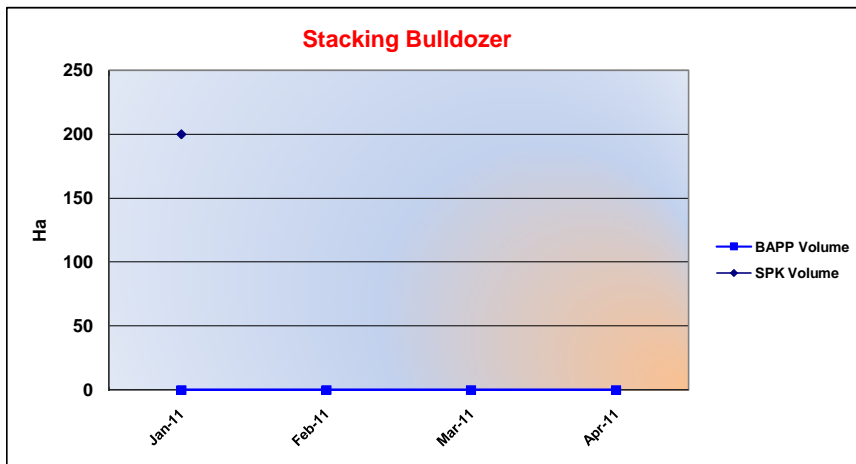

Month	Monthly Progress	Accumulated
Jan-11	-	-
Feb-11	-	-
Mar-11	-	-
Apr-11	-	-
Total	-	-

Type of Work	SPK Vol (Ha)	Progress	%
Stacking Excavator	500.00	126.82	25.36%

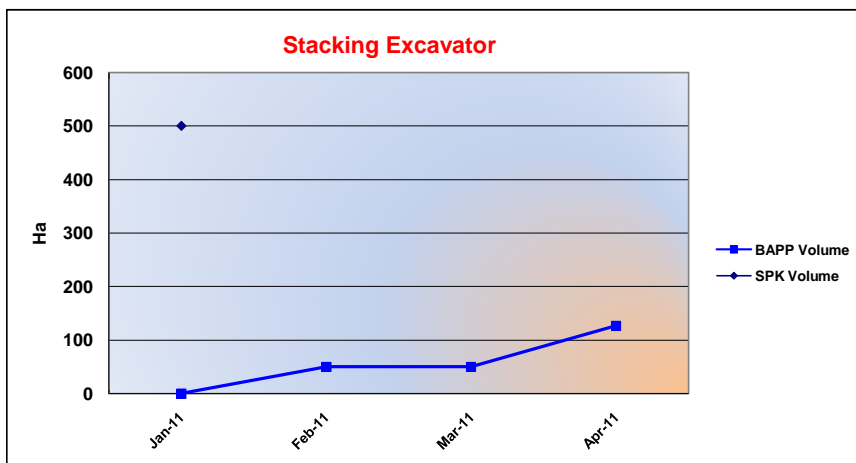


Month	Monthly Progress	Accumulated
Jan-11	-	-
Feb-11	49.90	49.90
Mar-11	-	49.90
Apr-11	76.92	126.82
Total	126.82	126.82



PT. RIMBA HARAPAN SAKTI


CLAIM SUMMARY

Type of Work	SPK Vol (Meter)	Progress	%
Road Formation 8 M	7,000.00	-	0.00%

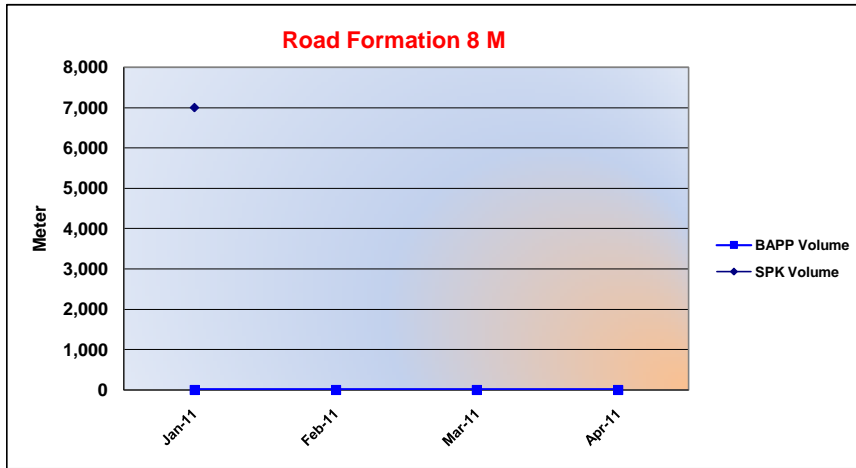


Month	Monthly Progress	Accumulated
Jan-11	-	-
Feb-11	-	-
Mar-11	-	-
Apr-11	-	-
Total	-	-

Type of Work	SPK Vol (Meter)	Progress	%
Road Formation 6 M	35,000.00	474.00	1.35%

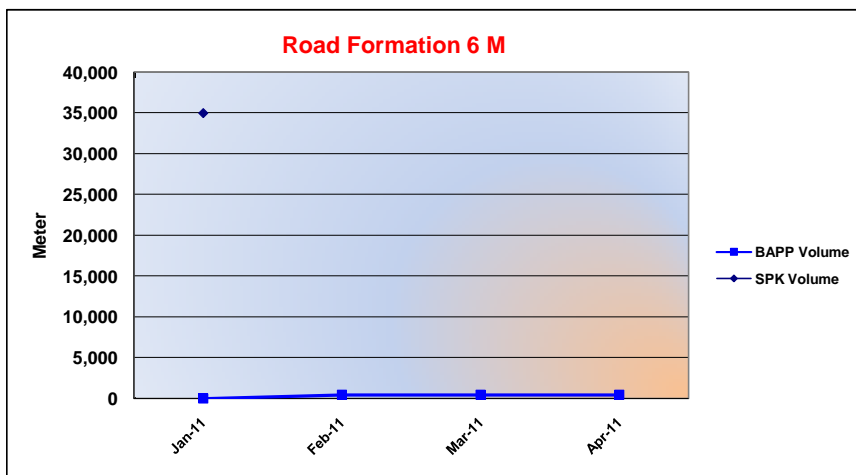

Month	Monthly Progress	Accumulated
Jan-11	-	-
Feb-11	474.00	474.00
Mar-11	-	474.00
Apr-11	-	474.00
Total	474.00	474.00

Type of Work	SPK Vol (Meter)	Progress	%
Main Drain 3,6x2,4x1,8	8,100.00	1,185.00	14.63%

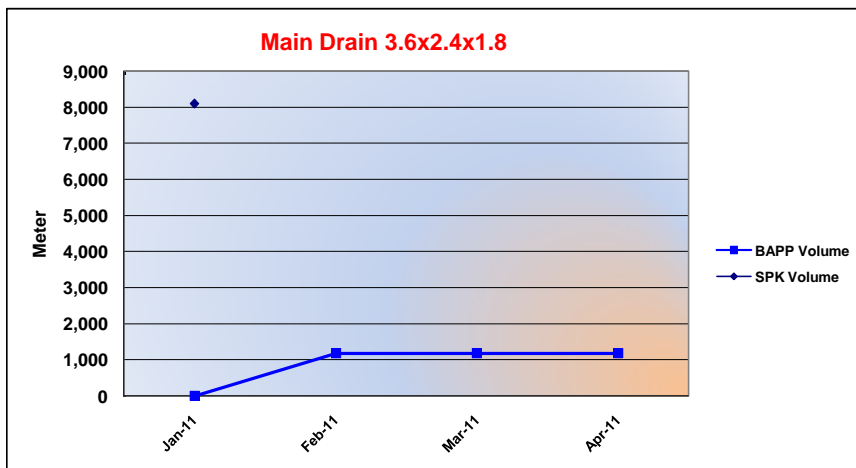


Month	Monthly Progress	Accumulated
Jan-11	-	-
Feb-11	1,185.00	1,185.00
Mar-11	-	1,185.00
Apr-11	-	1,185.00
Total	1,185.00	1,185.00



PT. RIMBA HARAPAN SAKTI


CLAIM SUMMARY

Type of Work	SPK Vol (Meter)	Progress	%
Main Drain 2,4x1,8x1,2	27,000.00	9,329.00	34.55%

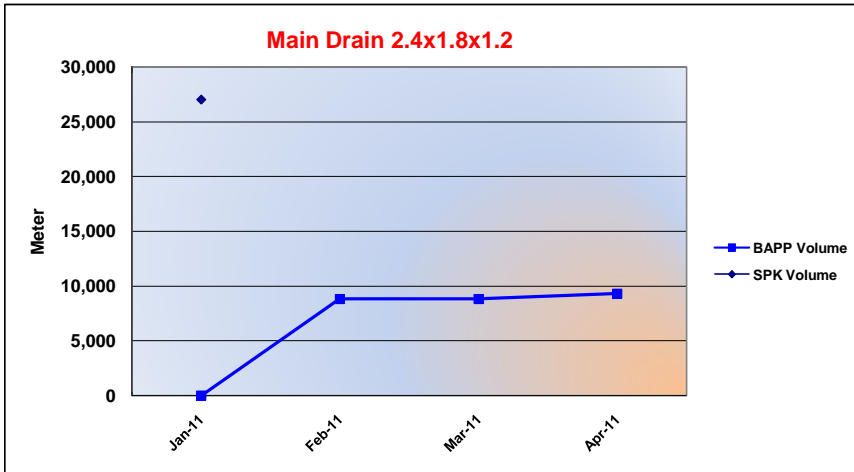


Month	Monthly Progress	Accumulated
Jan-11	-	-
Feb-11	8,847.00	8,847.00
Mar-11	-	8,847.00
Apr-11	482.00	9,329.00
Total	9,329.00	

Type of Work	SPK Vol (Meter)	Progress	%
Collection Drain 1,8x1,2x0,9	130,000.00	26,298.00	20.23%

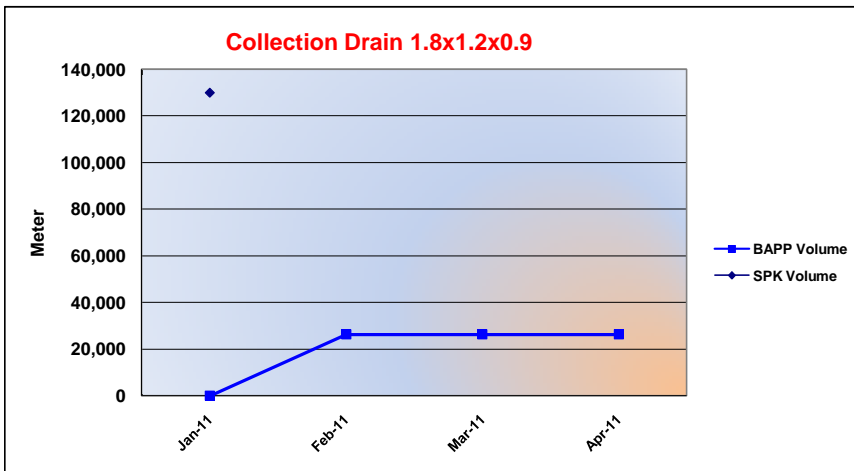

Month	Monthly Progress	Accumulated
Jan-11	-	-
Feb-11	26,298.00	26,298.00
Mar-11	-	26,298.00
Apr-11	-	26,298.00
Total	26,298.00	

Type of Work	SPK Vol (Meter)	Progress	%
Infield Drain 1,2x0,9x0,6	1,782,000.00	965,510.00	54.18%

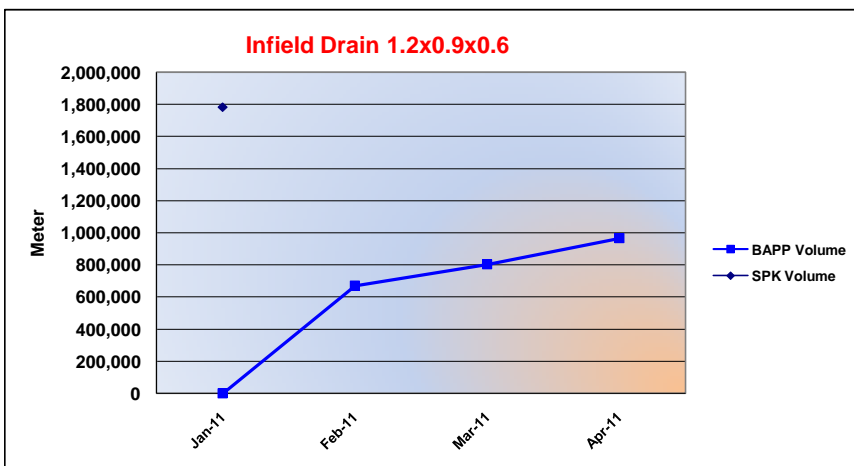


Month	Monthly Progress	Accumulated
Jan-11	-	-
Feb-11	671,001.00	671,001.00
Mar-11	132,594.00	803,595.00
Apr-11	161,915.00	965,510.00
Total	965,510.00	



PT. RIMBA HARAPAN SAKTI

CLAIM SUMMARY

Type of Work	SPK Vol (Ha)	Progress	%
Underbrushing (Imas)	700.00	538.34	76.91%

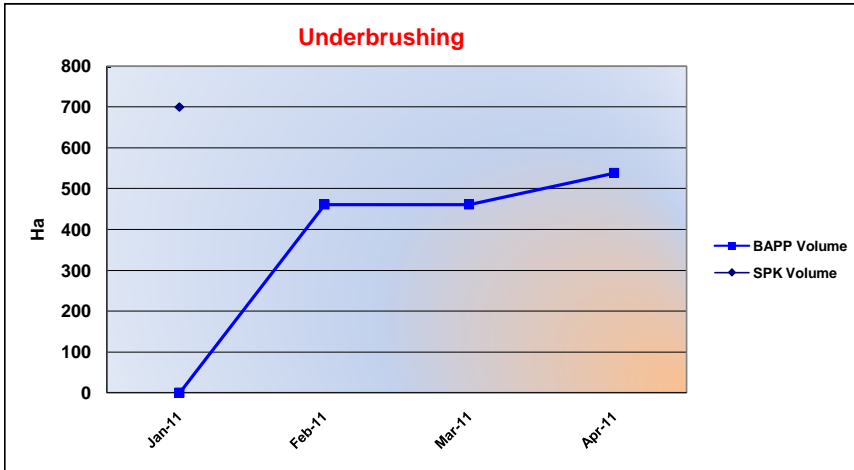

Month	Monthly Progress	Accumulated
Jan-11	-	-
Feb-11	461.42	461.42
Mar-11	-	461.42
Apr-11	76.92	538.34
Total	538.34	
