




**PROGRESS REPORT - Kebun Kawi**

KONTRAK NO :

- 1. 151/KAWE/JKTO/12/2012-Jalur Tanam, BPRT, & PJLN
- 2. 151/KAWE/JKTO/12/2012-SWAB

Jenis Pekerjaan	Unit	Vol SPK 1 Jan '13 s.d. 31 Des '13	Realisasi			%
			AKUMULASI S.D BULAN LALU	BAPP Juni 2013	S.D BAPP Juni 2013	
<b>Bulldozer</b>						
Jalur Tanam Darat	Ha	1.848,00	368,62	35,72	404,34	21,88%
Main Road Darat	Meter	16.402,00	1.949,56	791,90	2.741,46	16,71%
Collection Road Darat	Meter	54.029,00	4.789,52	1.199,80	5.989,32	11,09%
Jalan Contour	Meter	27.600,00	15.037,67	1.105,20	16.142,87	58,49%
Teras Contour	Meter	267.600,00	70.375,61	-	70.375,61	26,30%
Sewa Bulldozer	HM		1.595,40	1.379,60	2.975,00	
<b>Excavator</b>						
Jalur Tanam Rawa	Ha	552,00	276,50	101,40	377,90	68,46%
Parit 1 x 1 x 0,75	Meter	219.480,00	50.124,31	15.804,77	65.929,08	30,04%
Parit 2 x 2 x 1,5	Meter	37.027,00	11.205,39	3.975,81	15.181,20	41,00%
Parit 4 x 4 x 3	Meter	13.670,00	-	-	-	0,00%
Main Road Rawa	Meter	5.630,00	746,27	406,20	1.152,47	20,47%
Collection Road Rawa	Meter	18.547,00	3.407,61	2.780,38	6.187,99	33,36%
Gorong-gorong	Unit		8,00	5,00	13,00	
Jembatan 2 M	Unit		59,00	15,00	74,00	
Jembatan 4 M	Unit		-	-	-	
Jembatan 5-10 M	Unit		-	-	-	
Jembatan > 10 M	Unit		-	-	-	
Sewa Excavator	HM		4.081,80	1.512,70	5.594,50	
Imas Tumbang	Ha	2.400,00	-	-	-	0,00%

**Pekerjaan Bulldozer**

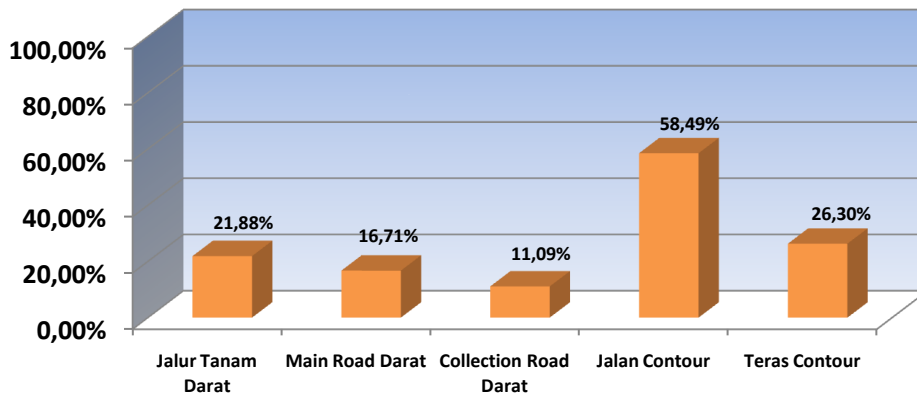

**Pekerjaan Excavator**

