




PROGRESS REPORT - Kebun HPM

KONTRAK NO :

1. 111868/HPM/SPK-PRO-HO/VIII/14

Jenis Pekerjaan	Unit	Vol SPK 25 Agt '14 s.d 31 Des' 15	Realisasi			%
			AKUMULASI S.D BULAN LALU	BAPP Juli 2015	S.D BAPP Juli 2015	
Bulldozer						
Imas Tumbang	Ha	1.168,00	-	13,42	13,42	1,15%
Stacking Darat	Ha	934,00	-	7,48	7,48	0,80%
Main Road - Darat	Meter	9.340,00	-	-	-	0,00%
Collection Road - Darat	Meter	31.130,00	-	-	-	0,00%
Jalan Contour	Meter	30.100,00	-	1.690,00	1.690,00	5,61%
Teras Contour	Meter	389.200,00	-	4.549,00	4.549,00	1,17%
Sewa Bulldozer	Hm	-	-	-	-	-
Excavator						
Stacking Rawa	Ha	530,00	-	4,95	4,95	0,93%
Parit 1x1x1	Meter	75.566,00	-	1.003,00	1.003,00	1,33%
Parit 2x2x1,5	Meter	-	-	-	-	0,00%
Parit 3x3x2,5	Meter	-	-	-	-	0,00%
Parit 4x4x2,5	Meter	-	-	-	-	0,00%
Main Road - Rawa	M ²	-	-	-	-	-
Collection Road - Rawa	M ²	-	-	-	-	-
Sewa Excavator	Hm	-	-	-	-	-
Jembatan 2 x 4	Unit	217,00	-	-	-	0,00%
Jembatan 3 x 4	Unit	-	-	-	-	0,00%
Jembatan 4 x 4	Unit	-	-	3,00	3,00	1,38%
Jembatan 6 x 4	Unit	-	-	-	-	0,00%

Pekerjaan Bulldozer

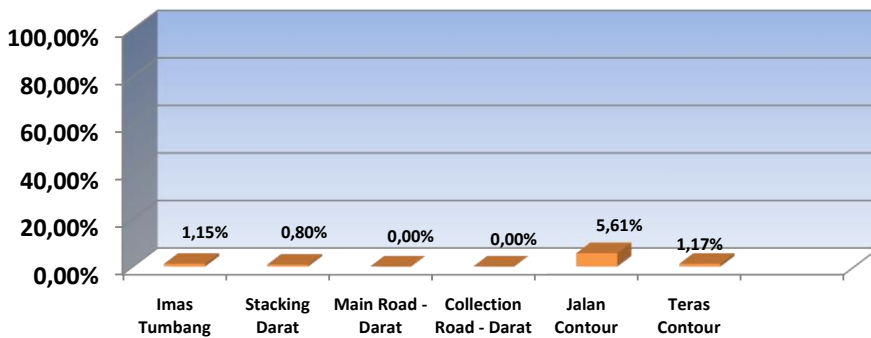

Pekerjaan Excavator

