




**PROGRESS REPORT - Kebun Sungai Biru**

KONTRAK NO :

1. 171/SBIE/LOA/12/2013 - BPRT, PJLN, Sewa
2. 007/SBIE/LOA/01/2014 - Gambangan

Jenis Pekerjaan	Unit	Vol SPK 1 Jan '14 s.d. 31 Des '14	Realisasi			%
			AKUMULASI S.D BULAN LALU	BAPP Feb 2014	S.D BAPP Feb 2014	
<b>Bulldozer</b>						
Jalur Tanam Darat	Ha	380,00	18,14	95,43	113,57	29,89%
Main Road Darat	Meter	408,00	-	-	-	0,00%
Collection Road Darat	Meter	1.344,00	-	-	-	0,00%
Jalan Contour	Meter	39.100,00	3.569,41	14.991,10	18.560,51	47,47%
Teras Contour	Meter	379.100,00	14.105,85	69.001,30	83.107,15	21,92%
Sewa Buldozer	HM		146,30	386,10	532,40	
<b>Excavator</b>						
Jalur Tanam Rawa	Ha	20,00	-	-	-	0,00%
Parit 1 x 1 x 0,75	Meter	10.900,00	-	-	-	0,00%
Parit 2 x 2 x 1,5	Meter	4.472,00	-	-	-	0,00%
Parit 4 x 4 x 3	Meter	404,00	-	-	-	0,00%
Main Road Rawa	Meter	204,00	-	-	-	0,00%
Collection Road Rawa	Meter	672,00	-	-	-	0,00%
Gorong-gorong	Unit		1,00	2,00	3,00	
Jembatan 2 M	Unit		-	4,00	4,00	
Jembatan 4 M	Unit		-	-	-	
Jembatan 5-10 M	Unit		-	-	-	
Jembatan > 10 M	Unit		-	-	-	
Sewa Excavator	HM		836,30	495,40	1.331,70	
Gambangan	Meter	876,00	-	-	-	
Imas Tumbang	Ha	400,00	-	-	-	0,00%

**Pekerjaan Bulldozer**

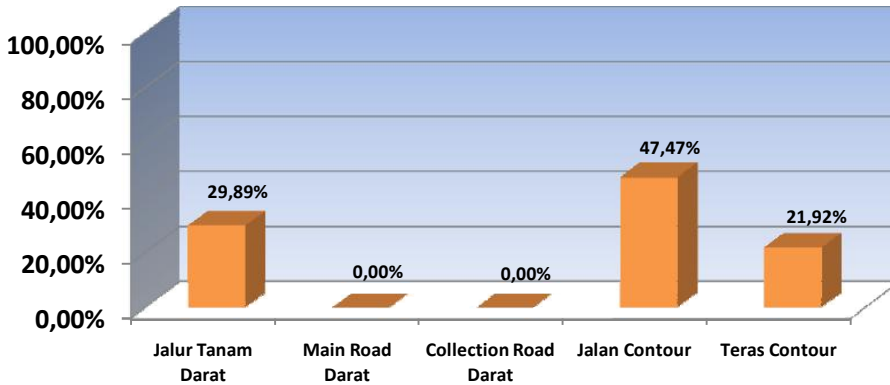

**Pekerjaan Excavator**

