



PT. PRIMABAHAGIA PERMAI


CLAIM SUMMARY - Bulungan Estate

Contract No. :

1. PBP/CR/084/07/2012

Type of Work	Unit	SPK Vol	Previous Month Claim	October '12 Claim	To Date Claimed	%
Bulldozer						
Perun Bulldozer	Ha	3.600,00	5,97	25,33	31,30	0,87%
Main Road 9 M	Meter	-	-	-	-	-
Main Road 7 M	Meter	48.000,00	4.012,00	389,00	4.401,00	9,17%
Collection Road 6 M	Meter	-	-	-	-	-
Collection Road 5 M	Meter	160.800,00	-	-	-	0,00%
Terracering 3,5 s/d 4,5 M	Meter	1.848.000,00	-	5.058,00	5.058,00	0,27%
Jalan Teras Kontour 5 M	Meter	160.776,00	26.152,00	6.732,00	32.884,00	20,45%
Sewa Buldozer	HM	-	217,90	155,90	373,80	-
Excavator						
Perun Excavator	Ha	900,00	-	-	-	0,00%
MR Tanggulan 9 M	Meter	12.000,00	-	-	-	0,00%
CR Tanggulan 7 M	Meter	40.200,00	-	-	-	0,00%
CR Tanggulan 6 M	Meter	-	-	-	-	-
CR Tanggulan 5 M	Meter	-	-	-	-	-
Parit 1 x 1 x 0,8	Meter	120.000,00	-	-	-	0,00%
Parit 2 x 2 x 1,5	Meter	60.000,00	-	-	-	0,00%
Parit 4 x 4 x 3	Meter	30.000,00	-	-	-	0,00%
Gorong-gorong	M ²	-	-	-	-	-
Jembatan	M ²	-	240,00	382,00	622,00	-
Sewa Excavator	HM	-	93,00	116,00	209,00	-
Imas Tumbang	Ha	4.500,00	-	125,68	125,68	2,79%

Bulldozer Work

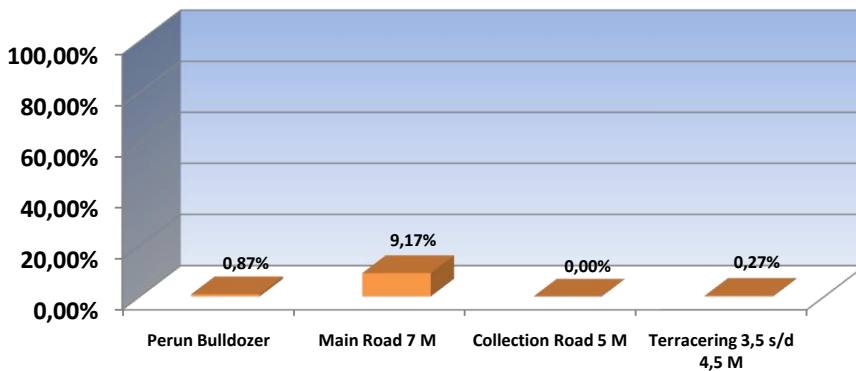

Excavator Work

