



# PT. BORNEO SAWIT PERDANA


## PROGRESS REPORT - Kebun Terantang

KONTRAK NO :


1. SPK No. TRTE/JKTO/026/04/2012-PL
2. SPK No. TRTE/JKTO/027/04/2012-SWAB

Jenis Pekerjaan	Unit	Vol SPK 02 Mei 2012 s.d 30 April 2014	Realisasi			%
			AKUMULASI S.D BULAN LALU	BAPP Sept 2012	S.D BAPP Sept 2012	
<b>Bulldozer</b>						
Perun Mekanis Darat	Ha	-	-	-	-	-
Main Road Darat	Meter	-	-	-	-	-
Collection Road Darat	Meter	-	-	-	-	-
Sewa Bulldozer	HM	-	-	-	-	-
<b>Excavator</b>						
Perun Mekanis Rawa	Ha	4.000,00	145,97	34,32	180,29	4,51%
Parit 1 x 1 x 0,75	Meter	970.000,00	2.636,94	607,45	3.244,39	0,33%
Parit 2 x 2 x 1,5	Meter	174.000,00	4.765,00	2.008,34	6.773,34	3,89%
Parit 4 x 4 x 3	Meter	40.000,00	2.377,58	-	2.377,58	5,94%
Main Road Rawa	Meter	40.000,00	3.423,43	2.008,34	5.431,77	13,58%
Collection Road Rawa	Meter	134.000,00	6.731,19	4.090,12	10.821,31	8,08%
Gorong-gorong 1 M	Unit	-	1,00	-	1,00	-
Jembatan Kayu 2 M	Unit	-	-	-	-	-
Jembatan Kayu 4 M	Unit	-	-	-	-	-
Jembatan Kayu 5-10 M	Unit	-	-	-	-	-
Sewa Excavator	HM	-	446,00	224,00	670,00	-

**Pekerjaan Bulldozer**



**Pekerjaan Excavator**

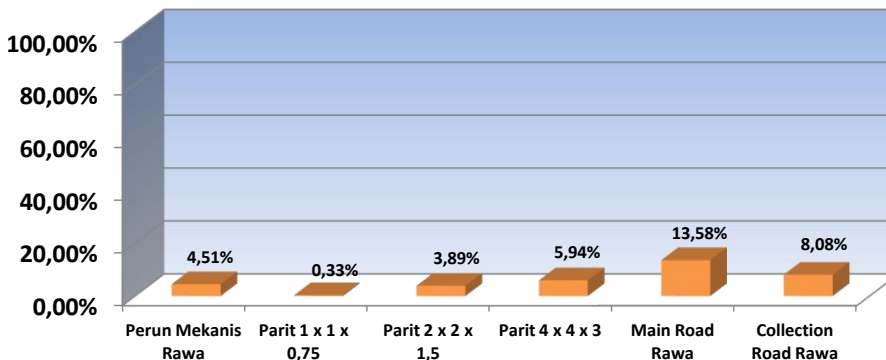






# PT. BORNEO SAWIT PERDANA

## PROGRESS REPORT - Kebun Terantang


Jenis Pekerjaan	Unit	Vol SPK	Realisasi	%
Sewa Bulldozer	HM	-	-	0,00%

Bulan	Hasil per Bulan	Kumulatif
Jun-12	-	-
Jul-12	-	-
Aug-12	-	-
Sep-12	-	-
	-	-

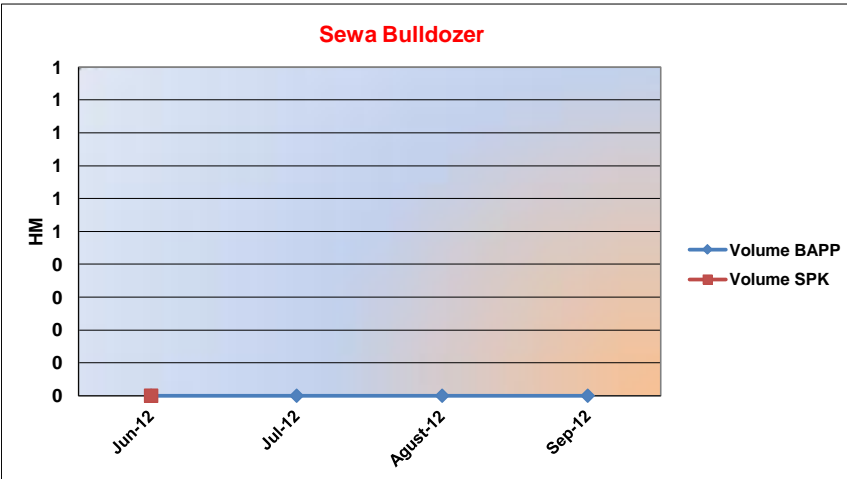


Jenis Pekerjaan	Unit	Vol SPK	Realisasi	%
Perun Mekanis Rawa	Ha	4.000,00	180,29	4,51%

Bulan	Hasil per Bulan	Kumulatif
Jun-12	11	11
Jul-12	61	72,11
Aug-12	74	145,97
Sep-12	34	180,29
	180	

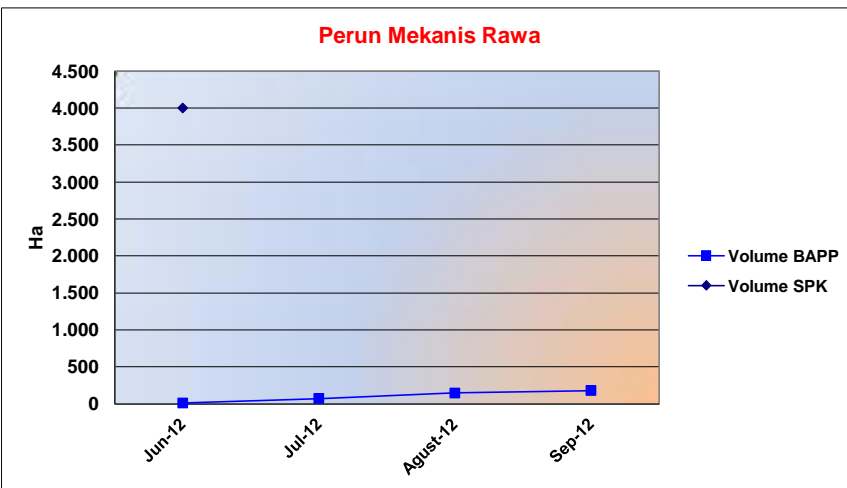

Jenis Pekerjaan	Unit	Vol SPK	Realisasi	%
Parit 1 x 1 x 0,75	Meter	970.000,00	3.244,39	0,33%

Bulan	Hasil per Bulan	Kumulatif
Jun-12	1.569	1.569
Jul-12	692	2.261,16
Aug-12	376	2.636,94
Sep-12	607	3.244,39
	3.244	

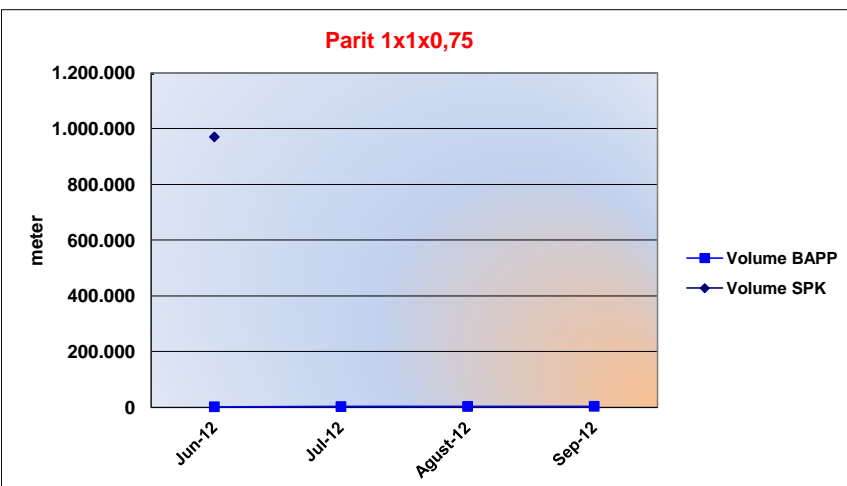




# PT. BORNEO SAWIT PERDANA

## PROGRESS REPORT - Kebun Terantang


Jenis Pekerjaan	Unit	Vol SPK	Realisasi	%
Parit 2 x 2 x 1,5	Meter	174.000,00	6.773,34	3,89%

Bulan	Hasil per Bulan	Kumulatif
Jun-12	1.902	1.902
Jul-12	2.713	4.614,81
Aug-12	150	4.765,00
Sep-12	2.008	6.773,34
	6.773	

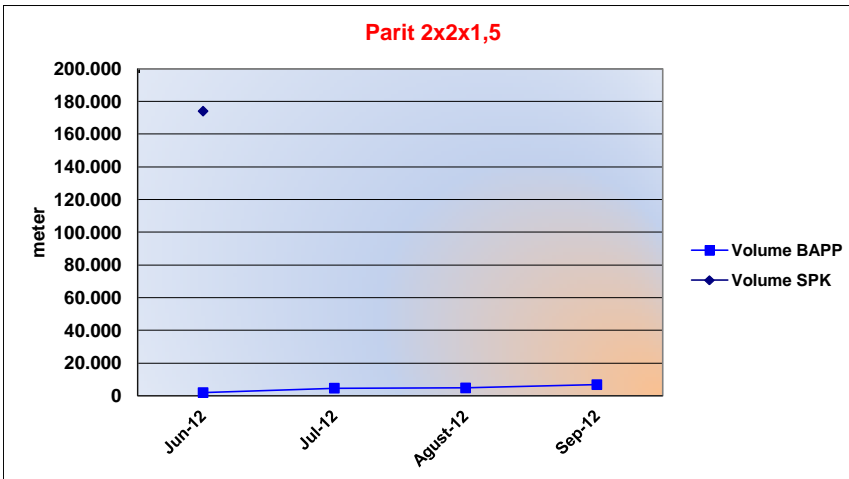


Jenis Pekerjaan	Unit	Vol SPK	Realisasi	%
Parit 4 x 4 x 3	Meter	40.000,00	2.377,58	5,94%

Bulan	Hasil per Bulan	Kumulatif
Jun-12	371	371
Jul-12	2.006	2.377,58
Aug-12	-	2.377,58
Sep-12	-	2.377,58
	2.378	

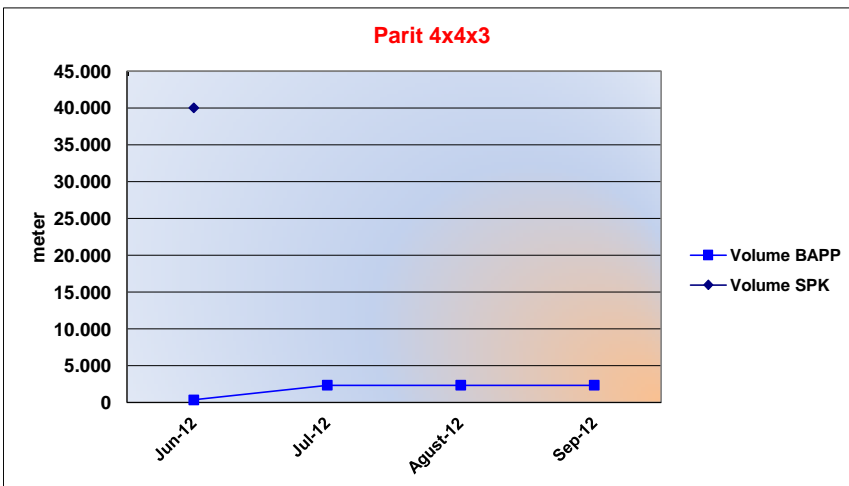

Jenis Pekerjaan	Unit	Vol SPK	Realisasi	%
Main Road Rawa	Meter	40.000,00	5.431,77	13,58%

Bulan	Hasil per Bulan	Kumulatif
Jun-12	1.889	1.889
Jul-12	1.385	3.273,24
Aug-12	150	3.423,43
Sep-12	2.008	5.431,77
	5.432	

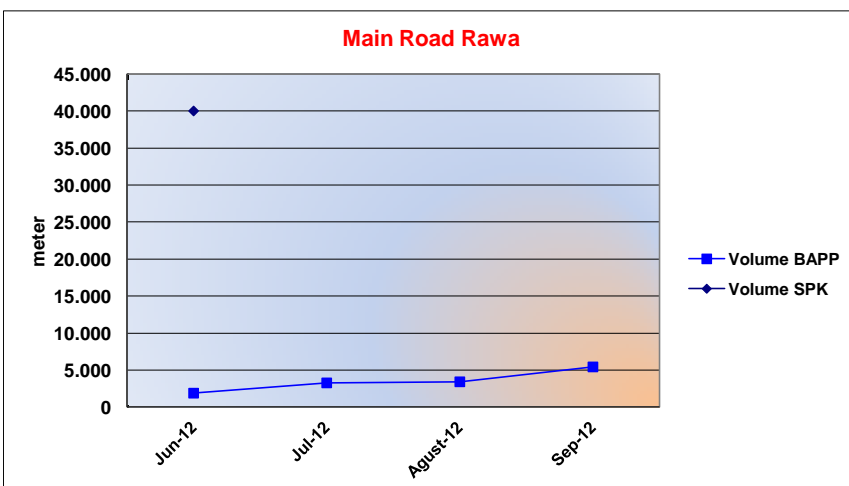




# PT. BORNEO SAWIT PERDANA

## PROGRESS REPORT - Kebun Terantang


Jenis Pekerjaan	Unit	Vol SPK	Realisasi	%
Collection Road Rawa	Meter	134.000,00	10.821,31	8,08%

Bulan	Hasil per Bulan	Kumulatif
Jun-12	753	753
Jul-12	5.785	6.538,38
Aug-12	193	6.731,19
Sep-12	4.090	10.821,31
	10.821	

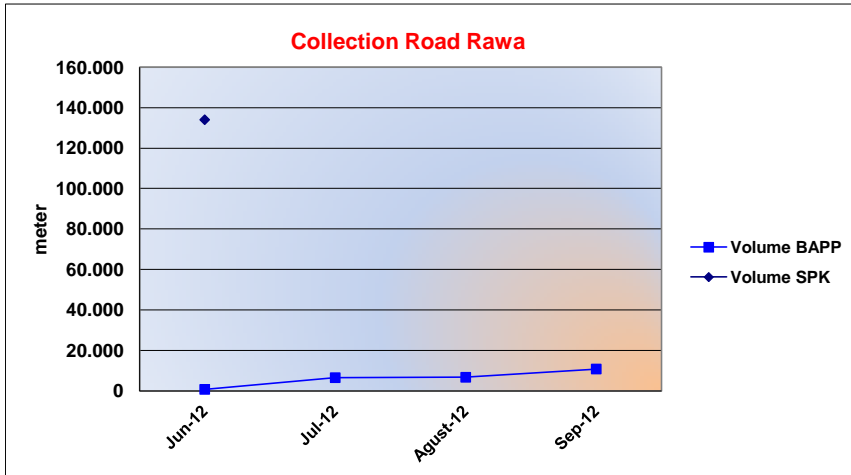


Jenis Pekerjaan	Unit	Vol SPK	Realisasi	%
Gorong-gorong 1 M	Unit	-	1,00	0,00%

Bulan	Hasil per Bulan	Kumulatif
Jun-12	1	1
Jul-12	-	1,00
Aug-12	-	1,00
Sep-12	-	1,00
	1	

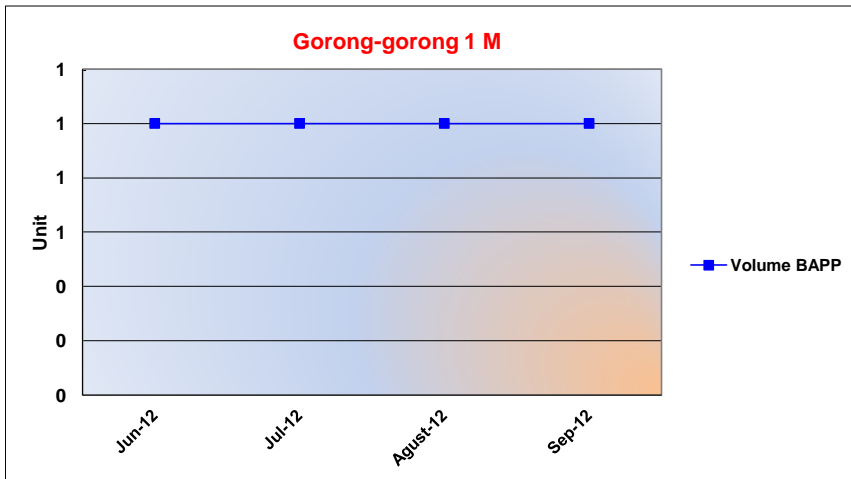

Jenis Pekerjaan	Unit	Vol SPK	Realisasi	%
Jembatan Kayu 2 M	Unit	-	-	0,00%

Bulan	Hasil per Bulan	Kumulatif
Jun-12	-	-
Jul-12	-	-
Aug-12	-	-
Sep-12	-	-
	-	

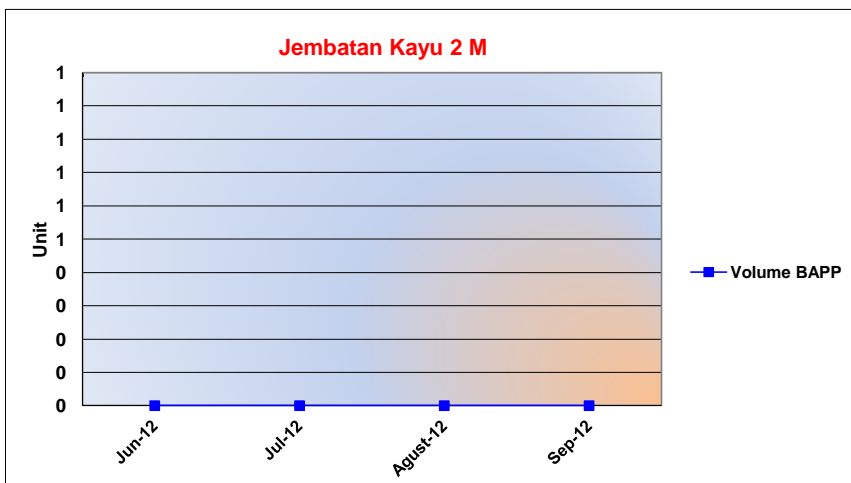




# PT. BORNEO SAWIT PERDANA


## PROGRESS REPORT - Kebun Terantang

Jenis Pekerjaan	Unit	Vol SPK	Realisasi	%
Jembatan Kayu 4 M	Unit	-	-	0,00%

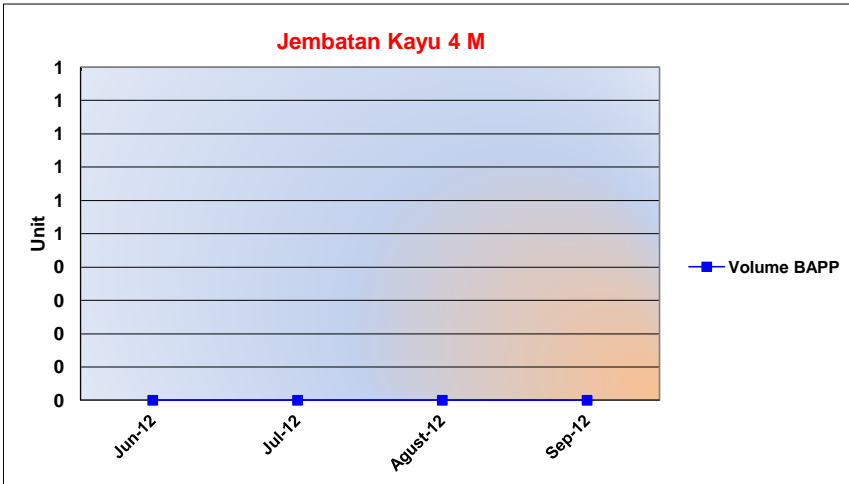


Bulan	Hasil per Bulan	Kumulatif
Jun-12	-	-
Jul-12	-	-
Aug-12	-	-
Sep-12	-	-
	-	-

Jenis Pekerjaan	Unit	Vol SPK	Realisasi	%
Jembatan Kayu 5-10 M	Unit	-	-	0,00%

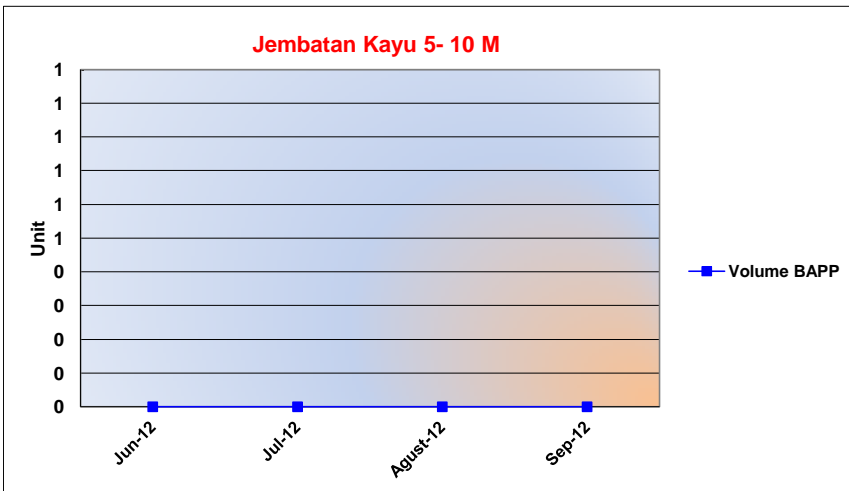

Bulan	Hasil per Bulan	Kumulatif
Jun-12	-	-
Jul-12	-	-
Aug-12	-	-
Sep-12	-	-
	-	-

Jenis Pekerjaan	Unit	Vol SPK	Realisasi	%
Sewa Excavator	HM	-	-	0,00%

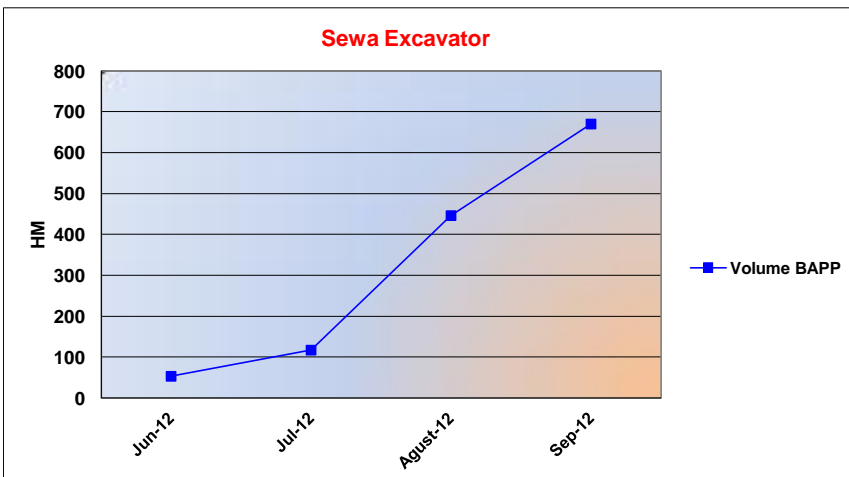

Bulan	Hasil per Bulan	Kumulatif
Jun-12	53	53
Jul-12	64	117,00
Aug-12	329	446,00
Sep-12	224	670,00
	670	
