



PT. NUSANTARA SAWIT PERSADA


PROGRESS REPORT - Kebun CEMPAGA

KONTRAK NO :

1. CMPE/JKTO/008/02/2015-PL

Jenis Pekerjaan	Unit	Vol SPK 1 Jan 15 s.d 31 Des 2015	Realisasi			%
			AKUMULASI S.D BULAN LALU	BAPP Agt 2015	S.D BAPP Agt 2015	
Bulldozer						
Perun Mekanis Darat/Perun DZR	Ha	300,00	13,00	3,72	16,72	5,57%
MR Darat/Main Road 9 M	M	3.100,00	-	-	-	0,00%
CR Darat/Collection Road 7 M	M	10.100,00	-	-	-	0,00%
Excavator						
Parit 1 x 1 x 0,8	M	12.000,00	-	-	-	0,00%
Parit 2 x 2 x 1,5	M	6.000,00	-	-	-	0,00%
Parit 4 x 4 x 3,0	M	3.000,00	-	-	-	0,00%

Bulldozer Work

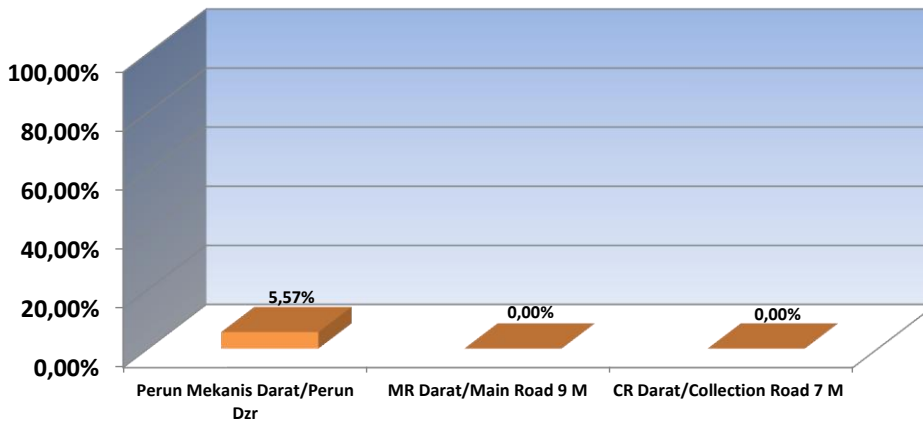

Excavator Work

