




PROGRESS REPORT - Kebun Gaharu

KONTRAK NO :

1. 066/GHRE/LOA/12/2013
2. 066/GHRE/JKTO/12/2013-PEMBUKAAN LAHAN
3. 066/GHRE/JKTO/12/2013-SWAB LP

Jenis Pekerjaan	Unit	Vol SPK 1 Jan '14 s.d. 31 Des '14	Realisasi			%
			AKUMULASI S.D BULAN LALU	BAPP Feb 2014	S.D BAPP Feb 2014	
Bulldozer						
Jalur Tanam Darat	Ha	900,00	11,64	18,02	29,66	3,30%
Main Road Darat	Meter	8.364,00	175,36	1.088,94	1.264,30	15,12%
Collection Road Darat	Meter	27.552,00	212,26	125,46	337,72	1,23%
Jalan Contour	Meter	14.950,00	-	-	-	0,00%
Teras Contour	Meter	144.950,00	1.121,83	1.449,27	2.571,10	1,77%
Sewa Buldozer	HM		189,00	124,00	313,00	
Excavator						
Jalur Tanam Rawa	Ha	50,00	0,86	-	0,86	1,72%
Parit 1 x 1 x 0,75	Meter	34.450,00	197,62	-	197,62	0,57%
Parit 2 x 2 x 1,5	Meter	11.180,00	178,86	-	178,86	1,60%
Parit 4 x 4 x 3	Meter	4.610,00	-	-	-	0,00%
Main Road Rawa	Meter	510,00	-	-	-	0,00%
Collection Road Rawa	Meter	1.680,00	-	-	-	0,00%
Gorong-gorong	Unit		-	-	-	
Jembatan 2 M	Unit		2,00	-	2,00	
Jembatan 4 M	Unit		1,00	-	1,00	
Jembatan 5-10 M	Unit		-	-	-	
Jembatan > 10 M	Unit		-	-	-	
Sewa Excavator	HM		74,00	4,00	78,00	
Imas Tumbang	Ha	950,00	-	-	-	0,00%

Pekerjaan Bulldozer

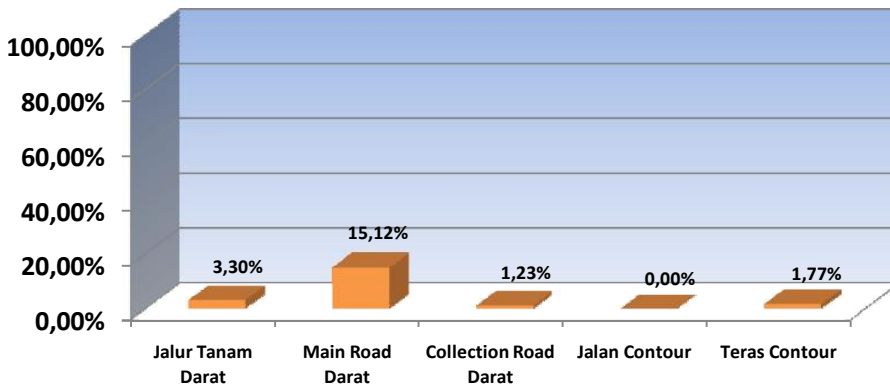

Pekerjaan Excavator

