



**PROGRESS REPORT - Kebun Persada**


KONTRAK NO :

1. NSP/JKTO/038/10/2013-PL

2. NSP/JKTO/043/10/2013-SWAB

Jenis Pekerjaan	Unit	Vol SPK 21 Okt 2013 s.d 31 Des 2014	Realisasi			%
			AKUMULASI S.D BULAN LALU	BAPP Feb 2014	S.D BAPP Feb 2014	
<b>Bulldozer</b>						
Perun Mekanis Darat	Ha	300,00	23,08	-	23,08	7,69%
Main Road Darat	Meter	3.100,00	292,00	-	292,00	9,42%
Collection Road Darat	Meter	11.000,00	741,00	-	741,00	6,74%
Sewa Bulldozer	HM		916,00	216,00	1.132,00	
<b>Excavator</b>						
Perun Mekanis Rawa	Ha	700,00	21,83	35,30	57,13	8,16%
Parit 1 x 1 x 0,75	Meter	40.000,00	46.433,00	2.615,00	49.048,00	122,62%
Parit 2 x 2 x 1,5	Meter	20.000,00	8.659,00	2.873,00	11.532,00	57,66%
Parit 4 x 4 x 3	Meter	10.000,00	1.447,00	932,00	2.379,00	23,79%
Main Road Rawa	Meter	7.200,00	-	3.585,00	3.585,00	49,79%
Collection Road Rawa	Meter	25.000,00	1.787,00	4.963,00	6.750,00	27,00%
Gorong-gorong 1 M	Unit	-	-	-	-	-
Jembatan Kayu 2 M	Unit	-	-	-	-	-
Jembatan Kayu 4 M	Unit	-	-	-	-	-
Jembatan Kayu 5-10 M	Unit	-	-	-	-	-
Sewa Excavator	HM	-	3.781,00	954,00	4.735,00	

**Pekerjaan Bulldozer**

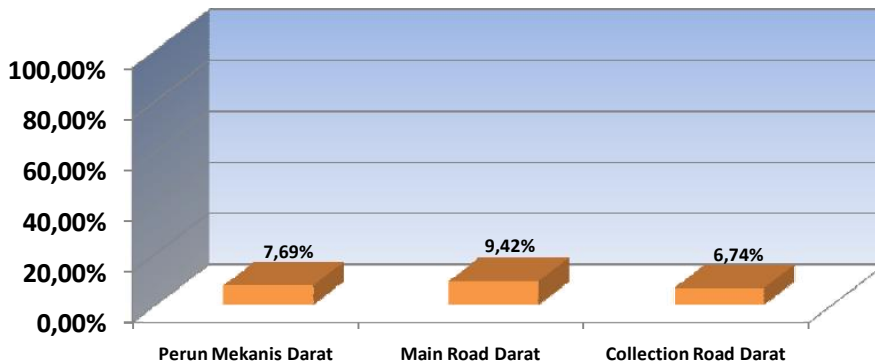

**Pekerjaan Excavator**

